


Emergency response in Lebanon

WINTERIZATION INTERVENTION IN BEKAA VALLEY



Activity report – 31st March 2013

Area of Intervention:

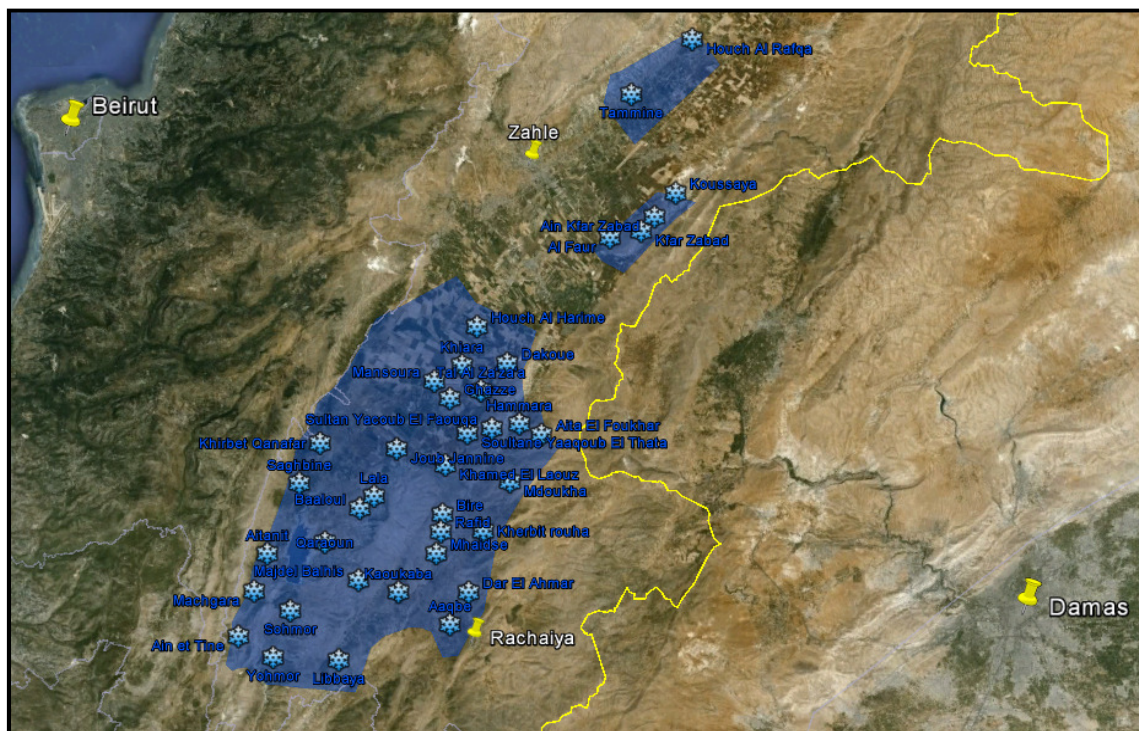

General monitoring:

Sealing off Kit WINTER						
HI Area / West & Central Bekaa	N° HI Assesment Shelter form by family	N° HI Family need sealinf off kit	% needed	N° Kit distributed/in progress	Kit completed sealing off HI	% Objective 650 families completed
Total	802	710	88,53%	710	710	109%
Ground isolation Kit WINTER						
HI Area / West & Central Bekaa	N° HI Assesment Shelter form by family	N° HI Family need Ground isolation kit	% needed	N° kit distributed/in progress	Kit completed Ground isolation HI	% Objective 650 families completed
Total	802	710	88,53%	702	702	108%
Heater Kit WINTER						
HI Area / West & Central Bekaa	N° HI Assesment Shelter form by family	N° HI Family need Heating kit	% needed	N° kit distributed/in progress	Kit completed Heater HI	% Objective 200 families completed
Total	802	191	23,82%	168	168	84%

Winterization technical details

Technical details shelter					
HI Area	N° Family need sealing off	Average Windows Sealing off needed / family	Average doors Sealing off needed / family	Average Carpet m2 / family	N° family NO heating
Total	695	1,95	0,99	7,07	182

Thermal indicator						
N° WINZH	Location	Date	Time	Outside °C *	Inside °C / before Winterization HI	Inside °C / after Winterization HI
WINZH-A-238	Saghbine	15/02/13	12h30	11,7 °C	12,5 °C	22,7 °C



Technical specification:


- **Specification sealing off kit:**
 - 1 Kit sealing off by family
 - 1 kit is composed by 4 sealing off windows, 1 sealing off door and accessories (1 foam bomb and 1 scotch roll, nails)

Service-provider:

- Each team by service provider can be composed by 2 carpenters + 2 labors

- All the materials was provided by Handicap International
- The transport of all materials done by the service provider.
- **Specification ground isolation kit:**
 - 1 ground isolation kit by family who benefited sealing off kit.
 - 1 ground isolation kit is composed by 20 m2 "moquette" fater 3 mm
 -
- **Specification stove kit:**
 - 1 heater kit by family
 - 1 heater kit is composed by 1 fuel stove + 1 reservoir + 3lm straight pipe + 2 corner pipe

Possible improvement "sealing off HI" during the spring/ summer:

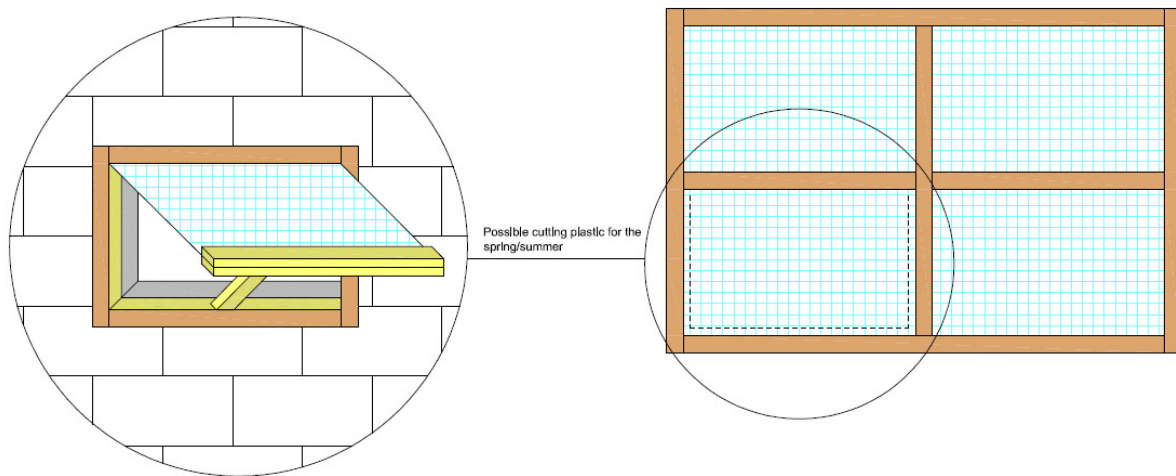

Contacts

Emergency Head of Mission: **Magalie Vairetto** hom.lb@hi-emergency.org / +961 78 89 89 25

Field coordinator Bekaa: **Andrew Merrat** / fielco.bk@hi-emergency.org / +961 78 81 53 93
